
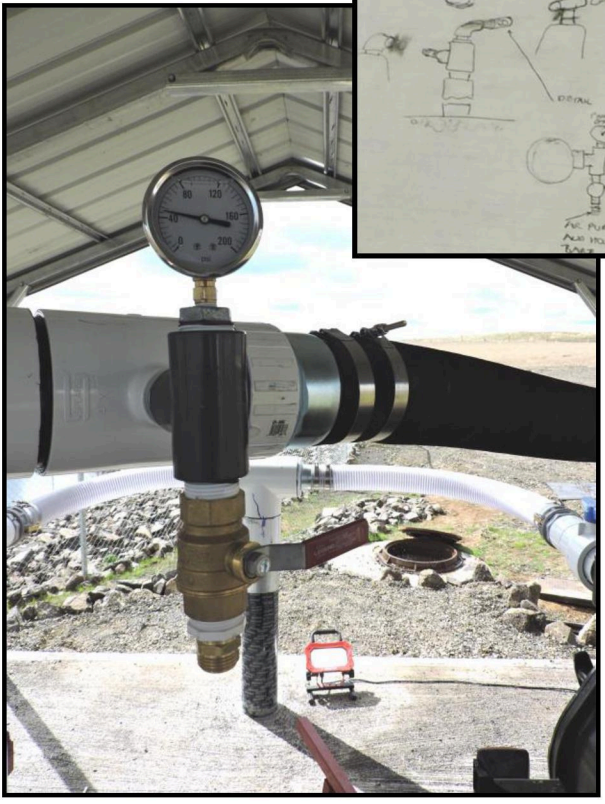
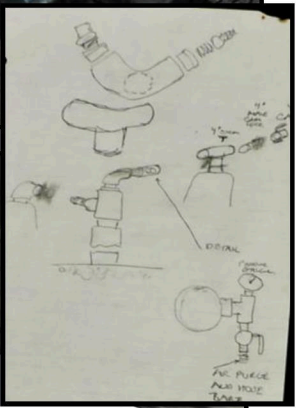


OREGON RACEWAY PARK

ONGOING PROJECTS UPDATE – 4/4/2016

The fire hydrant feed pumps are in and functional. One pump alone can run a 1.5 inch fire hose at both hydrants simultaneously and maintain 60 PSI of pressure. The 2,500 gallon tanker can take on a full load in about 5 minutes.

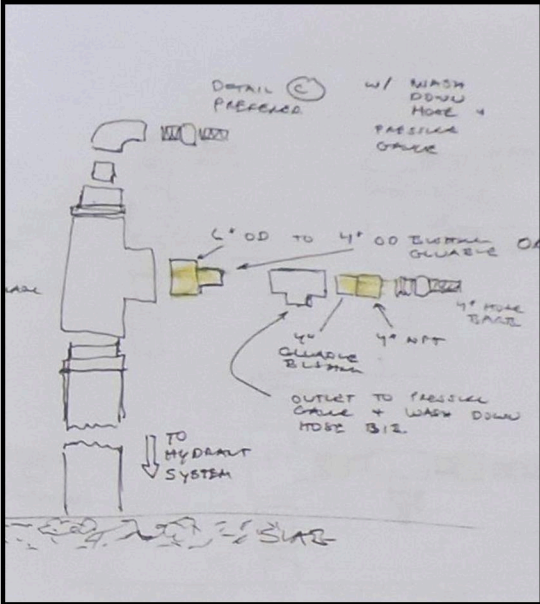

From "you know what would be good to have" to sketches to an up and roaring fire suppression system with double pump redundancy. Sometimes it doesn't take much to make a mechanic happy. It is one more milestone toward building out the track. The fresh water system should be done in a few days and the restrooms should be functional by the end of the month. Bill Murray
